


Project: Refurbishment Schedul Date: Wed 2/25/26	Task	[Red bar]	Inactive Task	[Grey bar]	Manual Summary Rollup	[Blue bar]	External Milestone	[Diamond]	Manual Progress	[Blue bar]
	Split	[Dotted bar]	Inactive Milestone	[Diamond]	Manual Summary	[Bracket]	Deadline	[Down arrow]		
	Milestone	[Diamond]	Inactive Summary	[Bracket]	Start-only	[C bar]	Critical	[Red bar]		
	Summary	[Bracket]	Manual Task	[Blue bar]	Finish-only	[J bar]	Critical Split	[Dotted bar]		
	Project Summary	[Bracket]	Duration-only	[Blue bar]	External Tasks	[Grey bar]	Progress	[Blue bar]		


ID	WBS	Task Name	Duration	M-1	M1	M2	M3	M4	M5	M6	M7	M8	M9	M10	M11	M12	M13	M14	M15	M16	M17	
42	1.2.1.4.4	Removal of Door and Windows	2 days																			
43	1.2.1.4.5	Removal of internal partitions	4 days																			
44	1.2.1.4.6	Removal of raised floors and floor finishes	5 days																			
45	1.2.1.4.7	Completion of soft strip on third floor	0 days																			
46	1.2.1.5	Soft Strip on Second Floor	15 days																			
47	1.2.1.5.1	Removal of false ceiling	2 days																			
48	1.2.1.5.2	Removal of outdated Electrical and Plumbing system	4 days																			
49	1.2.1.5.3	Removal of existing HVAC system	4 days																			
50	1.2.1.5.4	Removal of Door and Windows	2 days																			
51	1.2.1.5.5	Removal of internal partitions	4 days																			
52	1.2.1.5.6	Removal of raised floors and floor finishes	5 days																			
53	1.2.1.5.7	Completion of soft strip on second floor	0 days																			
54	1.2.1.6	Soft Strip on First Floor	15 days																			
55	1.2.1.6.1	Removal of false ceiling	2 days																			
56	1.2.1.6.2	Removal of outdated Electrical and Plumbing system	4 days																			
57	1.2.1.6.3	Removal of existing HVAC system	4 days																			
58	1.2.1.6.4	Removal of Door and Windows	2 days																			
59	1.2.1.6.5	Removal of internal partitions	4 days																			
60	1.2.1.6.6	Removal of raised floors and floor finishes	5 days																			
61	1.2.1.6.7	Completion of soft strip on first floor	0 days																			
62	1.2.1.7	Soft Strip on Mezzanine Floor	10 days																			
63	1.2.1.7.1	Removal of false ceiling	1 day																			
64	1.2.1.7.2	Removal of outdated Electrical and Plumbing system	3 days																			
65	1.2.1.7.3	Removal of existing HVAC system	2 days																			
66	1.2.1.7.4	Removal of Door and Windows	2 days																			
67	1.2.1.7.5	Removal of internal partitions	3 days																			
68	1.2.1.7.6	Removal of raised floors and floor finishes	3 days																			
69	1.2.1.7.7	Completion of soft strip on mezzanine floor	0 days																			
70	1.2.1.8	Soft Strip on Ground Floor	15 days																			
71	1.2.1.8.1	Removal of false ceiling	2 days																			
72	1.2.1.8.2	Removal of outdated Electrical and Plumbing system	4 days																			
73	1.2.1.8.3	Removal of existing HVAC system	4 days																			
74	1.2.1.8.4	Removal of Door and Windows	2 days																			
75	1.2.1.8.5	Removal of internal partitions	4 days																			
76	1.2.1.8.6	Removal of raised floors and floor finishes	5 days																			
77	1.2.1.8.7	Completion of soft strip on ground floor	0 days																			
78	1.2.1.9	Soft Strip on Basement Level 01	10 days																			
79	1.2.1.9.1	Removal of outdated Electrical and Plumbing system	3 days																			
80	1.2.1.9.2	Removal of existing HVAC system	4 days																			
81	1.2.1.9.3	Removal of Door and Windows	1 day																			
82	1.2.1.9.4	Removal of internal partitions	2 days																			
83	1.2.1.9.5	Removal of raised floors and floor finishes	5 days																			
84	1.2.1.9.6	Completion of soft strip basement level 01	0 days																			
85	1.2.1.10	Soft Strip on Basement Level 02	10 days																			

Project: Refurbishment Schedul
Date: Wed 2/25/26

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

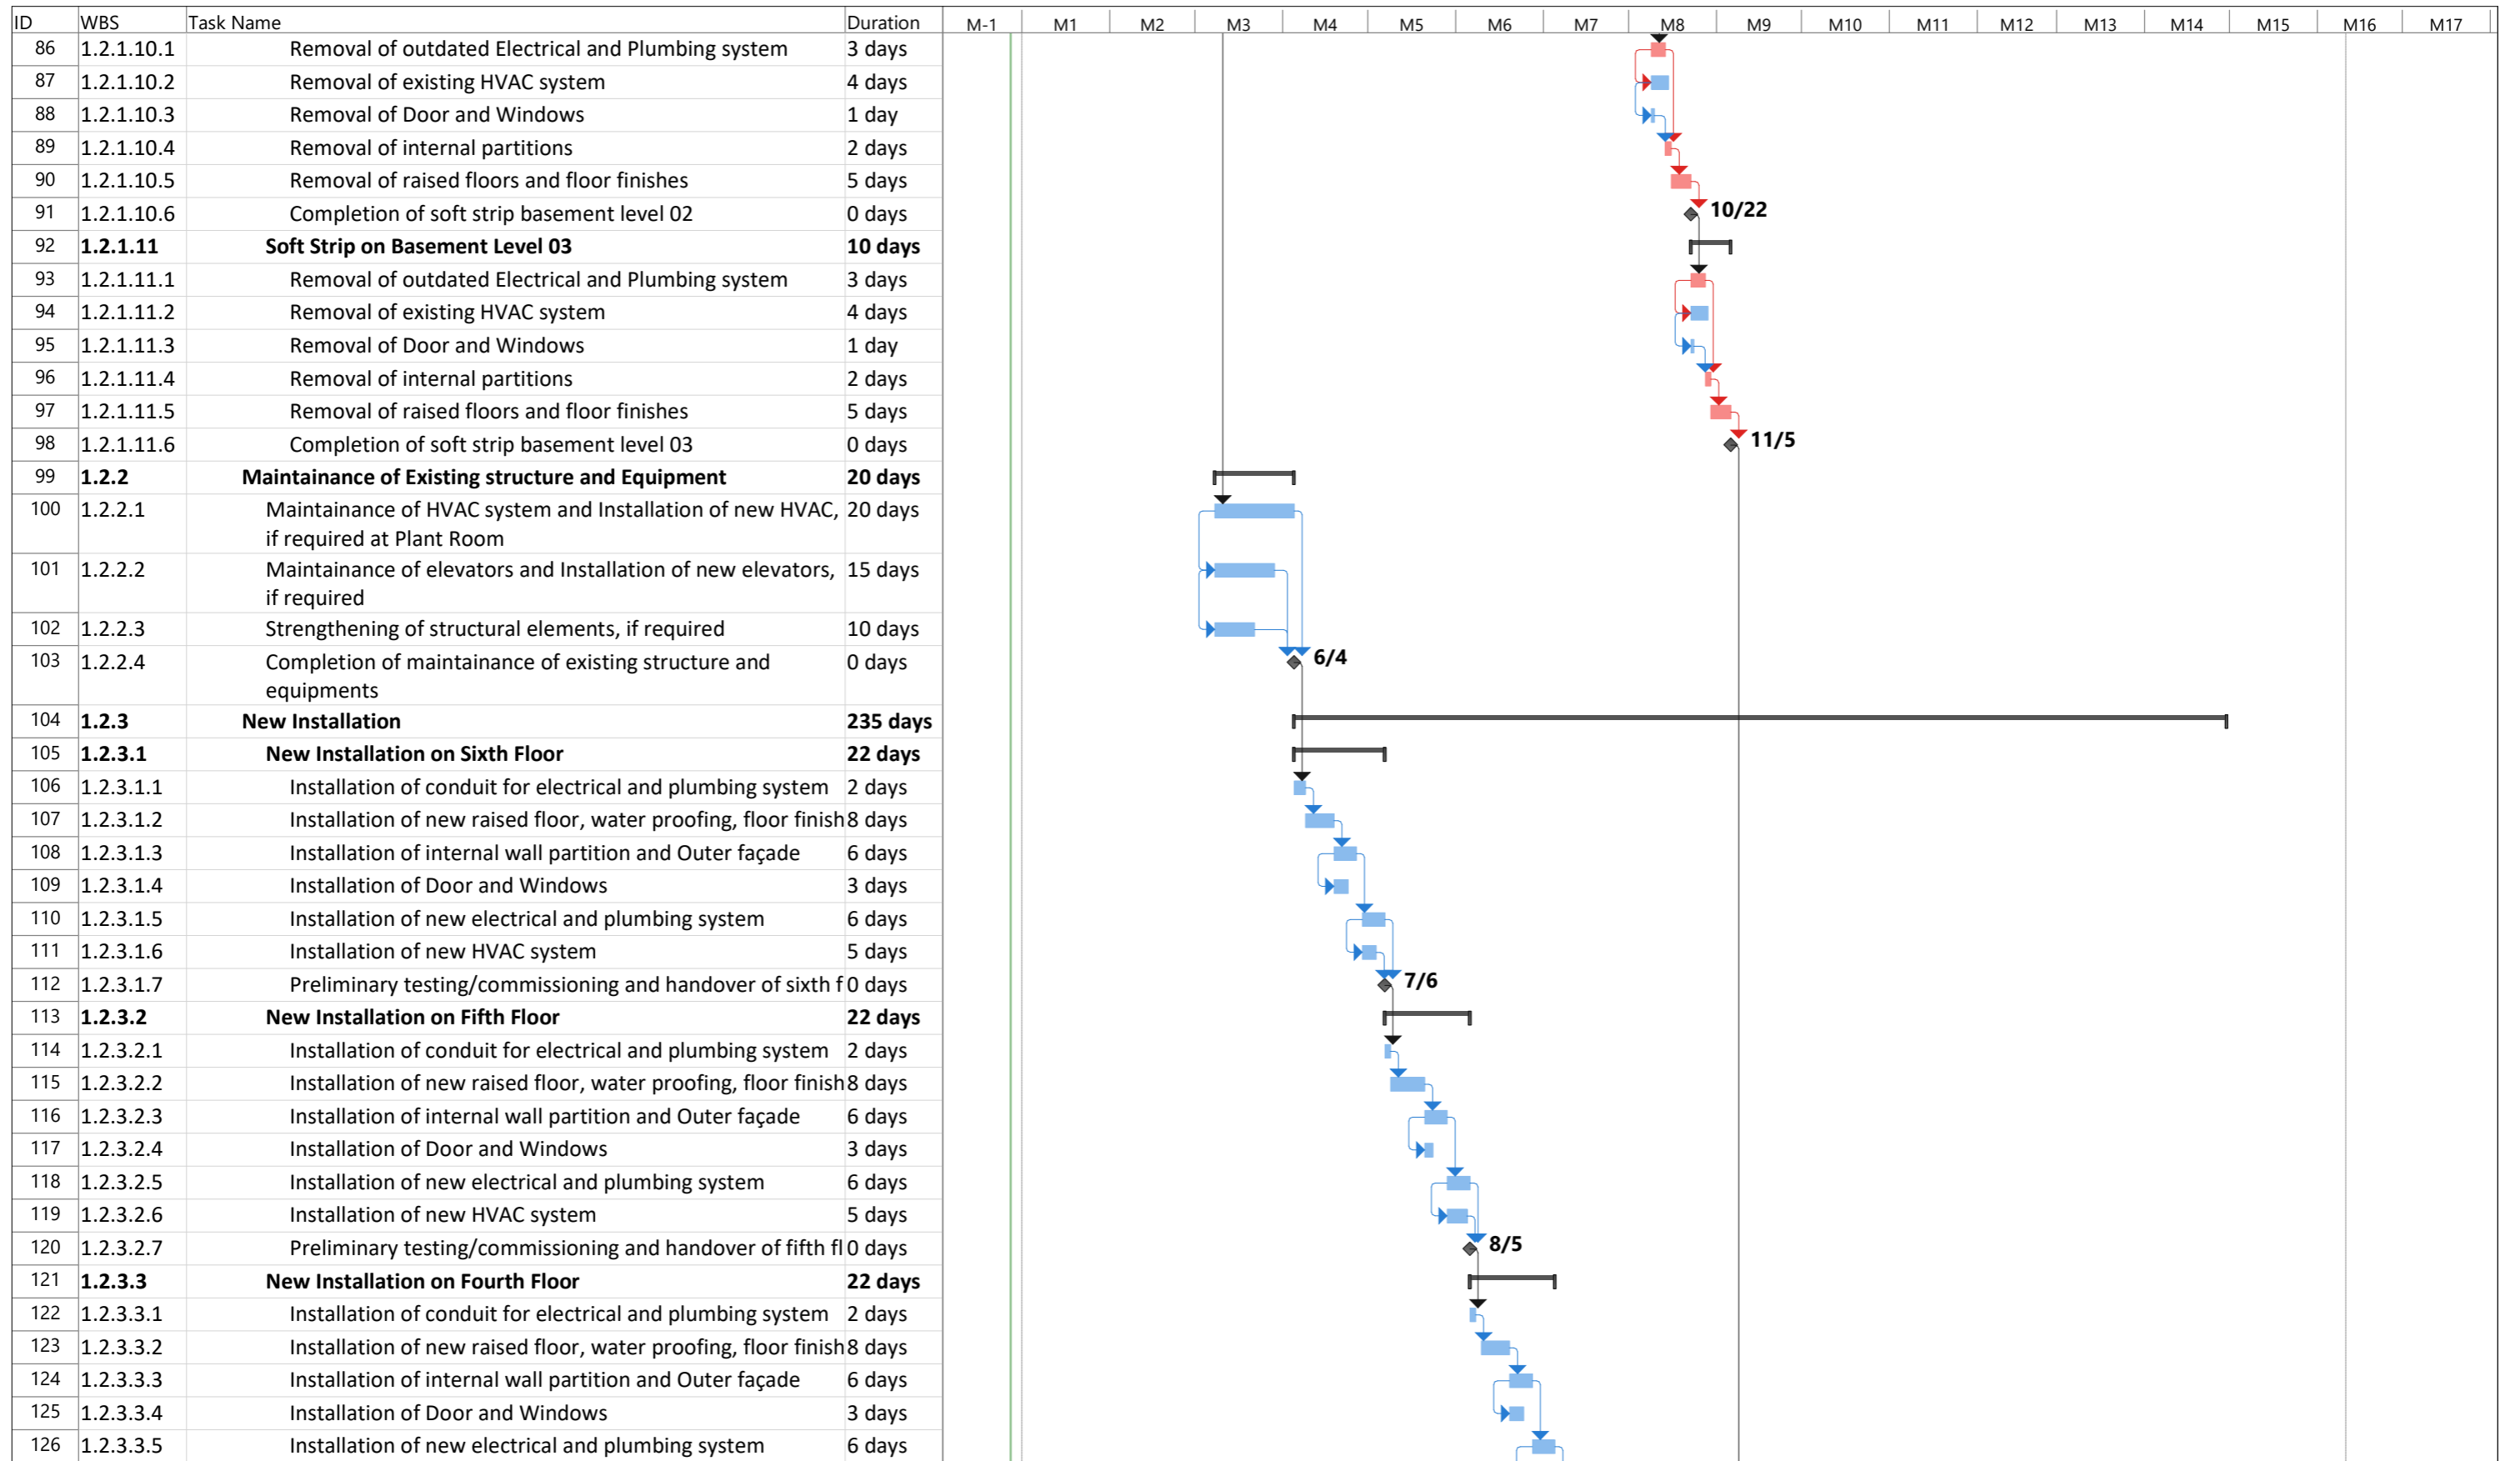


Project: Refurbishment Schedule Date: Wed 2/25/26	Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
	Split		Inactive Milestone		Manual Summary		Deadline			
	Milestone		Inactive Summary		Start-only		Critical			
	Summary		Manual Task		Finish-only		Critical Split			
	Project Summary		Duration-only		External Tasks		Progress			

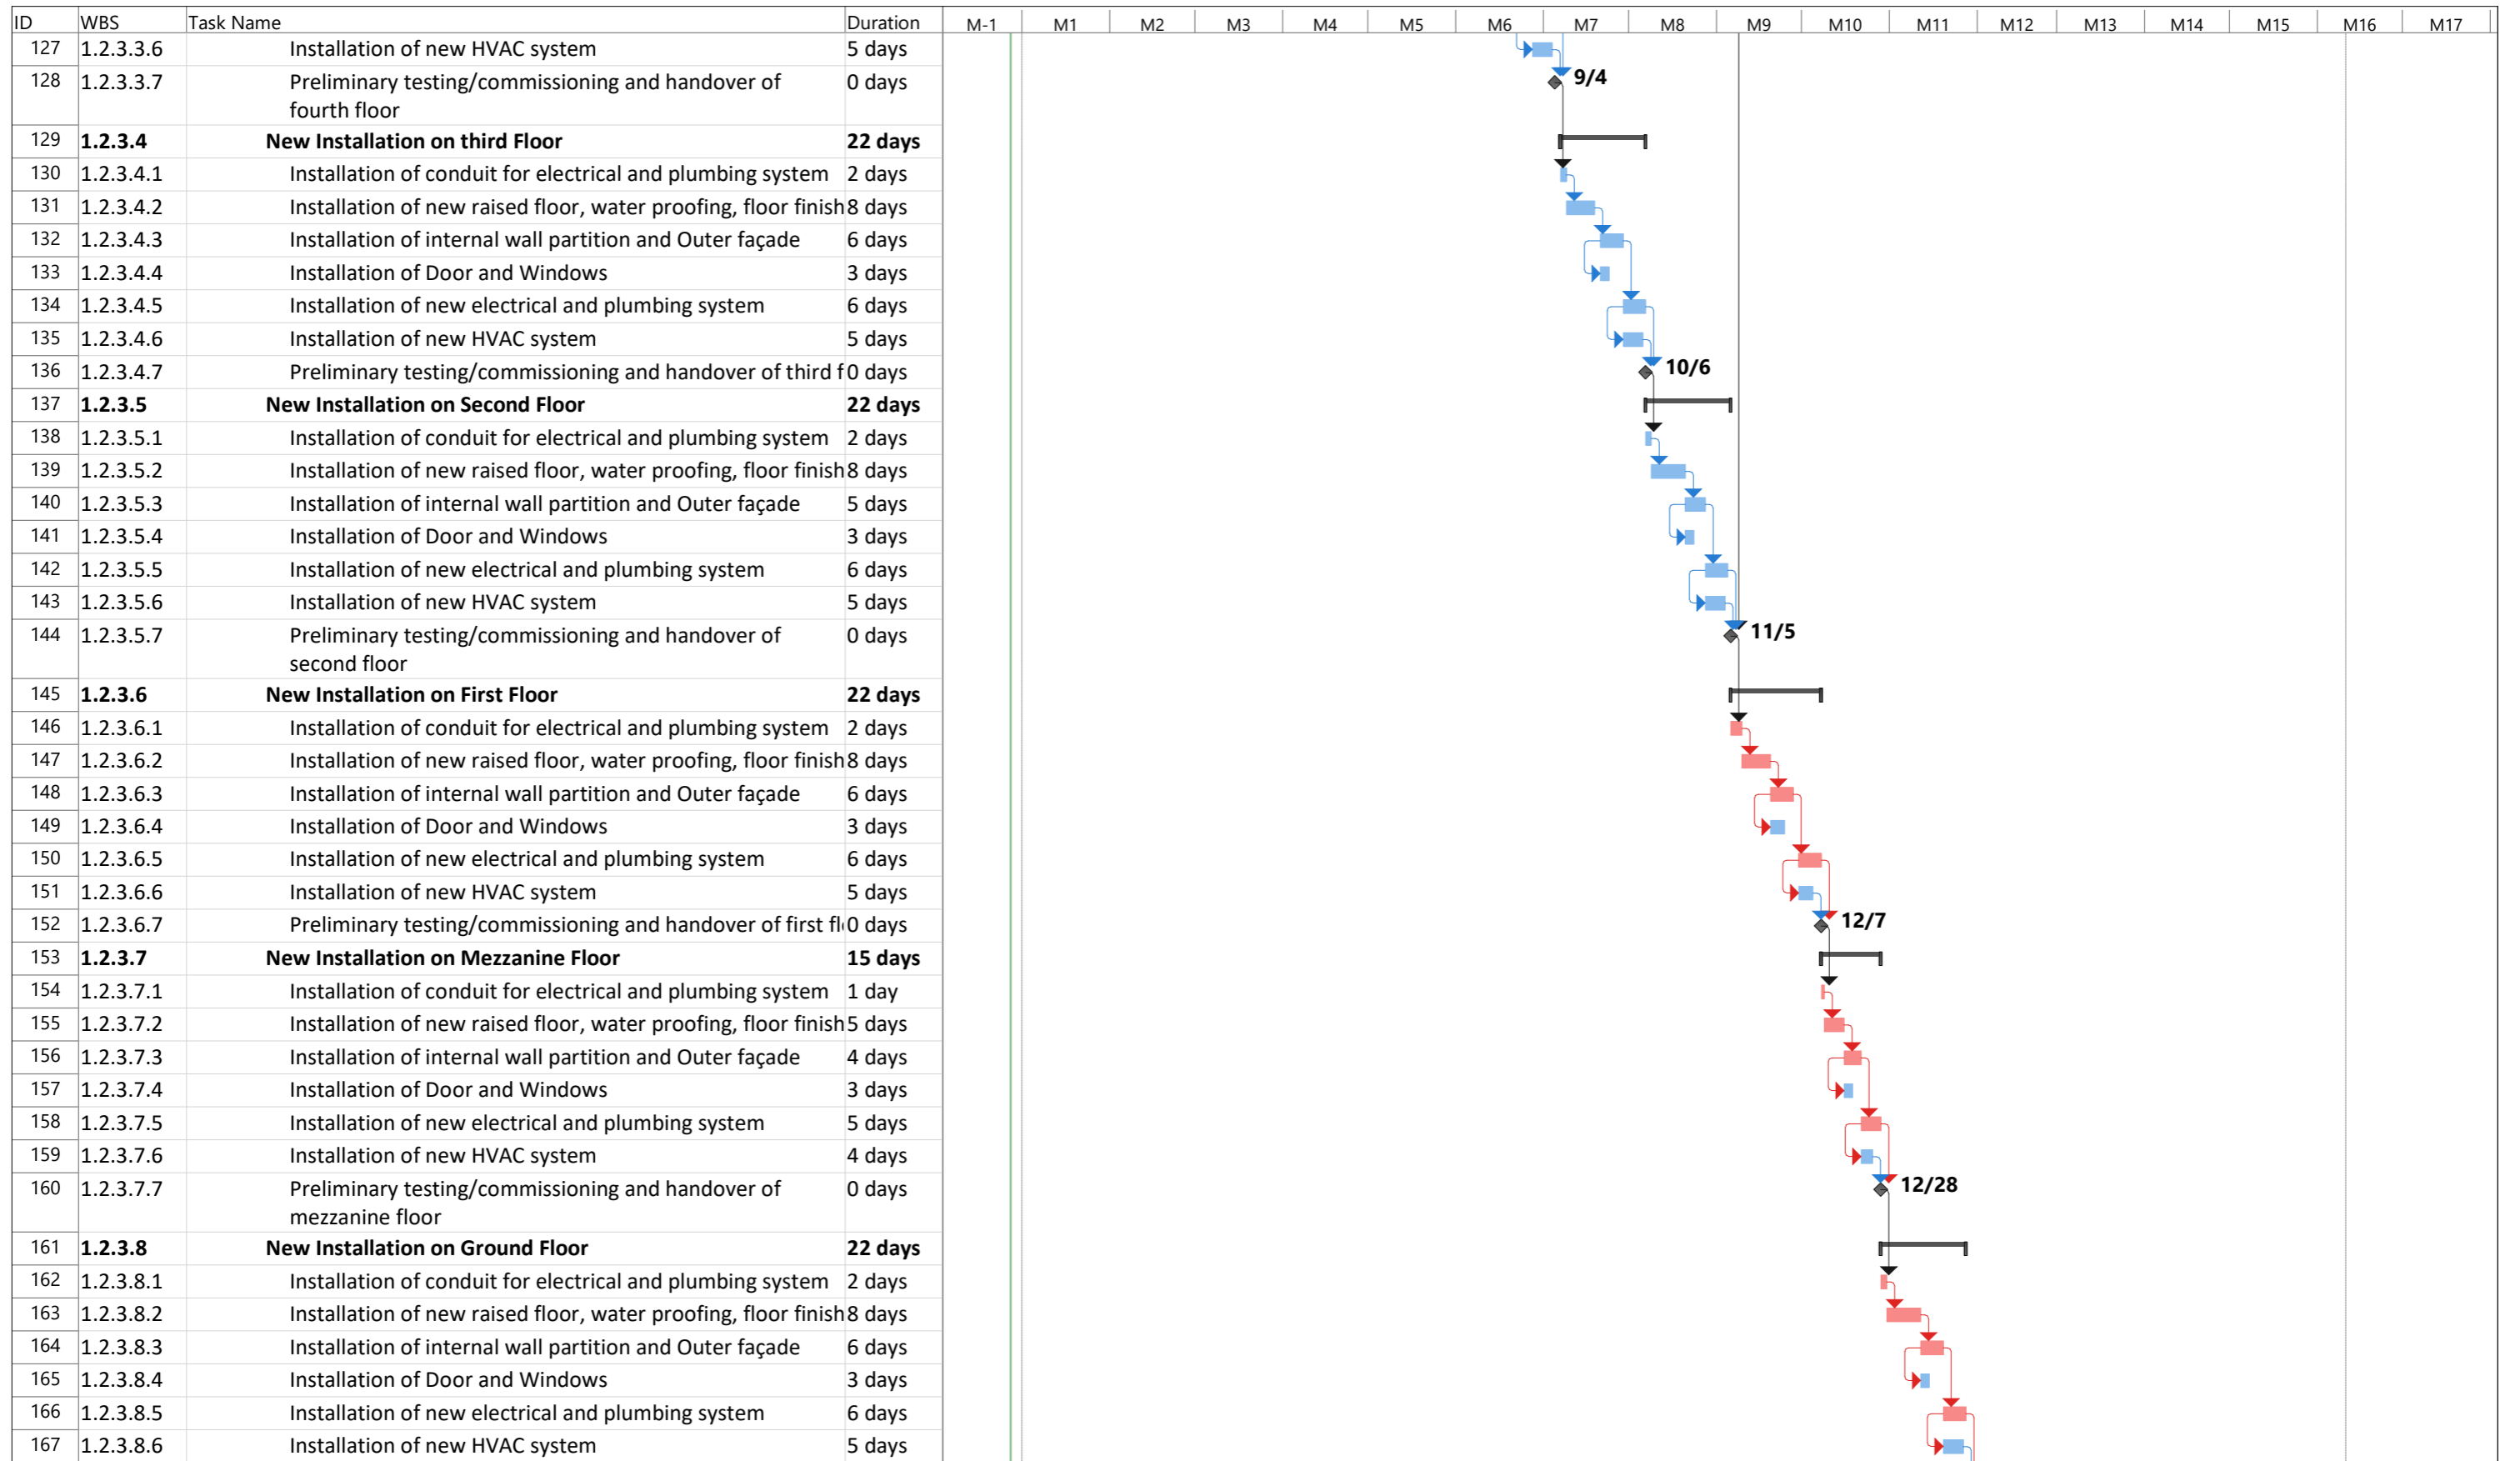

Project: Refurbishment Schedul Date: Wed 2/25/26	Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
	Split		Inactive Milestone		Manual Summary		Deadline			
	Milestone		Inactive Summary		Start-only		Critical			
	Summary		Manual Task		Finish-only		Critical Split			
	Project Summary		Duration-only		External Tasks		Progress			

ID	WBS	Task Name	Duration	M-1	M1	M2	M3	M4	M5	M6	M7	M8	M9	M10	M11	M12	M13	M14	M15	M16	M17
168	1.2.3.8.7	Preliminary testing/commissioning and handover of ground floor	0 days																		
169	1.2.3.9	New Installation on Basement Floor 01	22 days																		
170	1.2.3.9.1	Installation of conduit for electrical and plumbing system	2 days																		
171	1.2.3.9.2	Installation of new raised floor, water proofing, floor finish	8 days																		
172	1.2.3.9.3	Installation of internal wall partition and Outer façade	6 days																		
173	1.2.3.9.4	Installation of Door and Windows	3 days																		
174	1.2.3.9.5	Installation of new electrical and plumbing system	6 days																		
175	1.2.3.9.6	Installation of new HVAC system	5 days																		
176	1.2.3.9.7	Preliminary testing/commissioning and handover of basement floor level 01	0 days																		
177	1.2.3.10	New Installation on Basement Floor 02	22 days																		
178	1.2.3.10.1	Installation of conduit for electrical and plumbing system	2 days																		
179	1.2.3.10.2	Installation of new raised floor, water proofing, floor finish	8 days																		
180	1.2.3.10.3	Installation of internal wall partition and Outer façade	6 days																		
181	1.2.3.10.4	Installation of Door and Windows	3 days																		
182	1.2.3.10.5	Installation of new electrical and plumbing system	6 days																		
183	1.2.3.10.6	Installation of new HVAC system	5 days																		
184	1.2.3.10.7	Preliminary testing/commissioning and handover of basement floor level 02	0 days																		
185	1.2.3.11	New Installation on Basement Floor 03	22 days																		
186	1.2.3.11.1	Installation of conduit for electrical and plumbing system	2 days																		
187	1.2.3.11.2	Installation of new raised floor, water proofing, floor finish	8 days																		
188	1.2.3.11.3	Installation of internal wall partition and Outer façade	6 days																		
189	1.2.3.11.4	Installation of Door and Windows	3 days																		
190	1.2.3.11.5	Installation of new electrical and plumbing system	6 days																		
191	1.2.3.11.6	Installation of new HVAC system	5 days																		
192	1.2.3.11.7	Preliminary testing/commissioning and handover of basement floor level 03	0 days																		
193	1.3	Testing, Commissioning and Handover	30 days																		
194	1.3.1	Testing and commissioning of all system	7 days																		
195	1.3.2	Safety inspection	7 days																		
196	1.3.3	Punch list and defect correction	18 days																		
197	1.3.4	Final Inspection and Handover	5 days																		

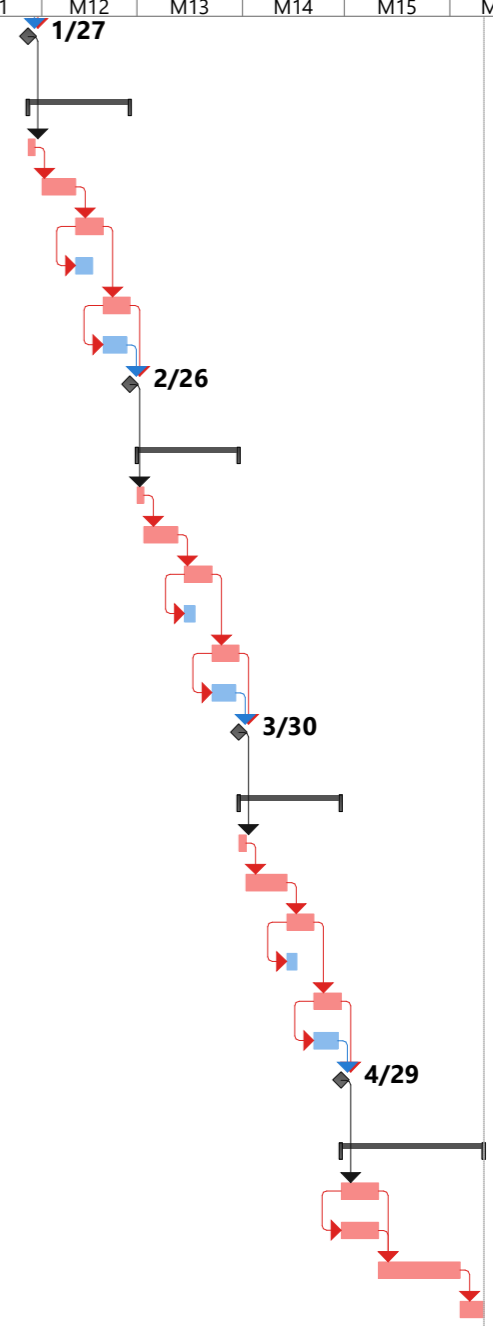

Project: Refurbishment Schedule Date: Wed 2/25/26	Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
	Split		Inactive Milestone		Manual Summary		Deadline			
	Milestone		Inactive Summary		Start-only		Critical			
	Summary		Manual Task		Finish-only		Critical Split			
	Project Summary		Duration-only		External Tasks		Progress			
